



West Africa Unique Identification for Regional Integration and Inclusion (WURI) Program (P161329)

WESTERN AND CENTRAL AFRICA | Western and Central Africa | IBRD/IDA | Investment Project Financing (IPF) | FY 2018 |
Seq No: 11 | Archived on 02-May-2025 | ISR03097

Implementing Agencies: ECOWAS Commission, Ministère de l'Emploi et de la Protection Sociale (CIV)

1. OBJECTIVE

1.1 Development Objective

Original Development Objective (Approved as part of Approval package on 09-Jan-2020)

The Program Development Objective (Pr.DO) is to increase the number of persons in participating countries who have government-recognized proof of unique identity that facilitates access to services.

The Project Development Objective (PDO) for Phase 1 of the Project is to increase the number of persons in Côte d'Ivoire and Guinea who have government-recognized proof of unique identity that facilitates access to services.

Has the Development Objective been changed since Board Approval of the Project Objective?

No

2. COMPONENTS

Name

Component 1: Strengthening the legal and institutional enabling environment:(Cost 9,600,000.00)

Component 2: Establishing robust and inclusive foundational ID systems:(Cost 100,850,000.00)

Component 3: Facilitating access to services through IDs:(Cost 11,650,000.00)

3. OVERALL RATINGS

Name	Previous	Current
Progress towards achievement of PDO	● Moderately Satisfactory	● Moderately Satisfactory
Overall Implementation Progress (IP)	● Moderately Satisfactory	● Satisfactory
Overall Risk Rating	● Substantial	● Substantial



4. KEY ISSUES & STATUS

4.1 Implementation Status and Key Decisions

Côte d'Ivoire. Through WURI, the Government of Ivory Coast aims to facilitate access to basic social services through identification, and improve the governance of social protection programs through interoperability between countries' systems. Implementation has improved steadily in the past 18 months. The project is hosted by the Ministry in charge of Social Protection (MEPS). WURI has partnered with the Universal Health Coverage Fund (CNAM) to roll out an inclusive, robust and no-cost functional ID system (subject to a restructuring) to facilitate access to social services and beyond. There is significant progress in enrollment in universal health insurance (Couverture maladie universelle, or CMU). Enrollment rates have increased from about 33 % of the population at the beginning of 2024 to about 60 % as of April 2025. There has also been progress on activities linked to the regulatory framework, which is part of the project's first component. This overall progress is reflected in an increase in disbursements from a low of 7 % at the beginning of the fiscal year 2024, to 38 % as of March 2025. The disbursement ratio is expected to reach 70 % by December 2025.

ECOWAS. Overall implementation progress has been satisfactory, with key strategic documents being drafted, and stakeholder workshops will be organized for their validation in the coming months. However, given the nature of the activities (elaborating regional wide and complex documents), disbursement by the ECOWAS commission has been lagging. A Priority Plan has been adopted to accelerate implementation and therefore disbursements, for the 14 months left in the project. The Priority Plan reorganizes project management and focuses on impactful activities. Key activities include WURI regional events (with a focus on learning and knowledge exchange), the stakeholder assessment and engagement plan, the adoption of a fID systems interoperability strategy, the adoption of a Community Act on electronic identification, a regional communications strategy, and a "fID to ENBIC" roadmap. The disbursement ratio is expected to reach 47 % by the end of this fiscal year.

Guinea. The World Bank and Guinea finalized the early closing of WURI-Guinea on June 28, 2024, two years ahead of the planned closing date of June 30, 2026. Phase 1 of the WURI MPA project was restructured in June 2024 to this end.

4.2 MPA Program Development Objective

Original MPA Program Development Objective (Approved as part of (Seq.) package on)

Current MPA Program Development Objective (Approved as part of (Seq.) package on)

4.3 Multiphase Programmatic Approach (MPA) Status (Public Disclosure)

The WURI Regional Program is structured as a Multiphase Programmatic Approach (MPA) operation. The MPA is an adaptive and programmatic approach that allows clients to structure a long, large or complex engagement as a set of linked operations (or phases) with intermediate, shorter-term objectives that contribute to an overall Program Development Objective (PrDO). The Program is regional, being built around the ECOWAS Free Movement Protocol and with regional integration ambitions, but it also takes a series of national perspectives, allowing countries (Benin, Burkina Faso, Cote d'Ivoire, Guinea, and Togo) to join overtime, and to join at different implementation levels insofar as they



subscribe to the same PrDO and take the same basic approach. The MPA is allowing—and encouraging—adjustments on the basis of learned implementation experience within the framework of the PrDO. Most importantly the MPA is also enabling the Bank to quickly respond to changing client needs and timing, while maintaining overall objectives and approach.

5. SYSTEMATIC OPERATIONS RISK-RATING TOOL

Risk Category	Rating at Approval Approval Package - 09 Jan 2020	Last Approved Rating ISR Seq. 09 - 03 Jan 2024	Proposed Rating
Political and Governance	● Substantial	● Substantial	● Substantial
Macroeconomic	● Moderate	● Moderate	● Moderate
Sector Strategies and Policies	● High	● Moderate	● Moderate
Technical Design of Project or Program	● High	● Moderate	● Moderate
Institutional Capacity for Implementation and Sustainability	● High	● Moderate	● Moderate
Fiduciary	● Substantial	● Moderate	● Substantial
Environment and Social	● Substantial	● Substantial	● Substantial
Stakeholders	● High	● Moderate	● Substantial
Other	● High	● Moderate	● Moderate
Overall	● High	● Substantial	● Substantial



6. RESULTS

6.1 PDO Indicators by PDO Outcomes

Legal robustness								
Indicator Name	Baseline		Actual (Previous)		Actual (Current)		Closing Period	
	Value	Month/Year	Value	Date	Value	Date	Value	Month/Year
The enabling legal and institutional framework for the development and support of the fID system is in place (Text)	No	Jul/2018	Partially	28-Jun-2024	Partially	30-Mar-2025	Yes	Jun/2026
	Comments on achieving targets		The institutional arrangements are consolidated in Cote d'Ivoire, yet not fully in Guinea. Specific to the laws, the process is ongoing in Cote d'Ivoire. The Client is considering additional legal instruments that will support the relevant existing identification laws. In Guinea, the National Transition Council passed a new personal identification legislation in october 2023 that casts uncertainty on its implications for Guinea's legal cadaster; A law was passed on identifying physical persons with a separate Law on the civil registry to support the anticipated Administrative census for civil registry purposes (Recensement administratif à vocation d'état civil, RAVEC). The texts adopted before the National Transition Council did not fully reflect the principles of identification for sustainable development .					
Technical robustness								
Indicator Name	Baseline		Actual (Previous)		Actual (Current)		Closing Period	
	Value	Month/Year	Value	Date	Value	Date	Value	Month/Year
Existence of a fID system which generates UNIs and is in alignment with international good practices (Text)	No	Jul/2018	Partial	28-Jun-2024	Not available yet	30-Mar-2025	Yes	Jun/2026
	Comments on achieving targets		A pilot was conducted in Guinea in 20XX. A Pilot has been launched in Cote d'Ivoire in June 2024.					
Inclusion and Coverage								



Indicator Name	Baseline		Actual (Previous)		Actual (Current)		Closing Period	
	Value	Month/Year	Value	Date	Value	Date	Value	Month/Year
Direct project beneficiaries who have received a UNI (of which women) (Number (Thousand))	0.00	Jul/2018	8.00	28-Jun-2024	0	30-Mar-2025	24,000.00	Jun/2026
	Comments on achieving targets		Through the Pilot in Guinea, 8000 persons received a UNI.					
Access to Services								
Indicator Name	Baseline		Actual (Previous)		Actual (Current)		Closing Period	
	Value	Month/Year	Value	Date	Value	Date	Value	Month/Year
Digital authentications made per month by service providers on behalf of their beneficiaries or clients (of which, women) (Number)	0.00	Jul/2018	0	28-Jun-2024	0	30-Mar-2025	500,000.00	Jun/2026
National or regional functional public and private services linked to the Foundational ID system (Number)	0.00	Jul/2018	0.00	28-Jun-2024	0.00	30-Mar-2025	2.00	Jun/2026
	Comments on achieving targets		Once the fID is functional, the Republic of Cote d'Ivoire intends to link it to at least three services					

6.2 Intermediate Results Indicators by Components

Component 1: Strengthening the legal and institutional enabling environment								
Indicator Name	Baseline		Actual (Previous)		Actual (Current)		Closing Period	
	Value	Month/Year	Value	Date	Value	Date	Value	Month/Year
	No	Jul/2018	No	28-Jun-2024	No	30-Mar-2025	Yes	Jun/2026



The law for the fID system has been adopted, establishing, inter alia, inclusivity for all persons in the country, issuance of UNIs, linking to the CR system, and assuring data protection and privacy (Text)	Comments on achieving targets		The project no long seeks to have a fID law adopted, but rather to widen the scope of the existing UHC law, to include/graft a digital identification platform that expands access to services beyond healthcare.					
Regular consultations held with beneficiaries, ID stakeholders, vulnerable groups and government to solicit feedback and report on actions taken to address feedback since prior consultations (Text)	No	Jul/2018	Yes	28-Jun-2024	Yes	30-Mar-2025	Consultations held every year.	Jun/2026
	Comments on achieving targets		Ongoing consultations with village-level leaders, administrative authorities, and other relevant stakeholders are ongoing on enrollment operations.					
Grievances responded to and/or resolved within the stipulated service standards for response times (Percentage)	0.00	Jul/2018	52	28-Jun-2024	80	30-Mar-2025	90.00	Jun/2026
	Comments on achieving targets		The number presented is that of the CNAM's GRM services database.					
Component 2: Establishing robust and inclusive foundational ID systems								
Indicator Name	Baseline		Actual (Previous)		Actual (Current)		Closing Period	
	Value	Month/Year	Value	Date	Value	Date	Value	Month/Year
Individuals in the fID system whose biometric and demographic data meet international quality standards (Percentage)	0.00	Jul/2018	0.00	28-Jun-2024	85	30-Mar-2025	50	Jun/2026
	Comments on achieving targets		This is based on CNAM's current data systems, and quality of biometrics, which are intended to inform the digital identification system.					




Newborn birth registrations that are assigned UNIs (of which girls) (Number of people)	0	Jul/2018	0.00	28-Jun-2024	0.00	30-Mar-2025	5,000,000	Jun/2026
Comments on achieving targets	Not relevant at this stage of the Project.							



7. DATA ON FINANCIAL PERFORMANCE

7.1 Cumulative Disbursements

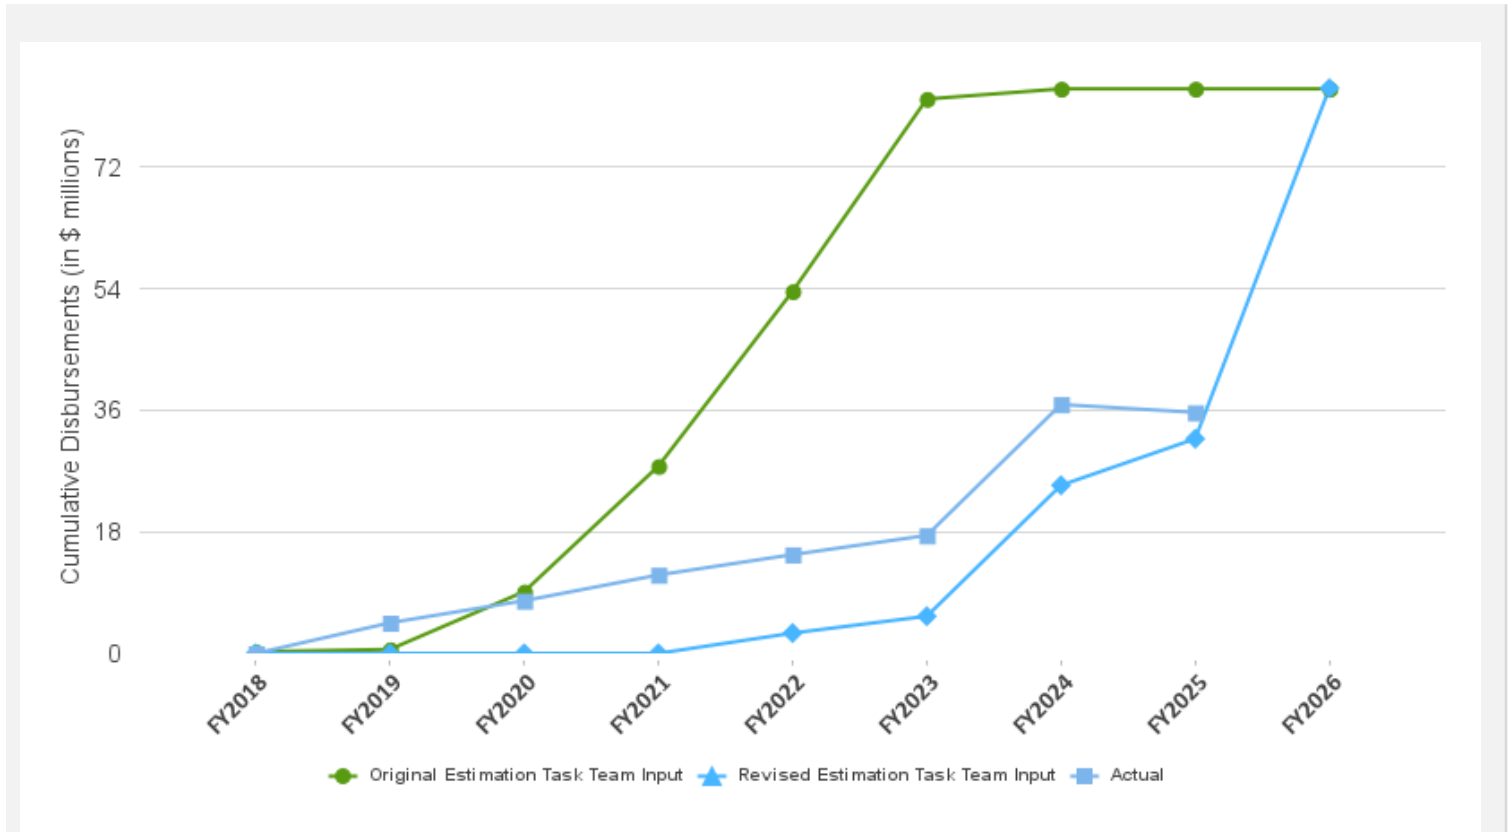

7.2 Disbursements (by loan)

Loan/Credit/TF	Status	Original	Revised	Cancelled	Disbursed	Undisbursed	% Disbursed
IDA-D3260	Closed	24.85	6.98	15.17	7.33	0.40	94.80%
IDA-D3210	Effective	5.00	4.55	0.00	1.78	2.83	38.65%
IDA-62400	Closed	24.85	4.86	17.33	4.39	1.16	79.03%
IDA-62390	Effective	67.40	59.41	0.00	22.16	37.31	37.26%

7.3 Key Dates (by loan)



Loan/Credit/TF	Status	Approval	Signing	Effectiveness	Orig. Closing	Rev. Closing
IDA-62390	Effective	05-Jun-2018	13-Jul-2018	09-Nov-2018	03-Jul-2024	30-Jun-2026
IDA-62400	Closed	05-Jun-2018	27-Jun-2018	20-Dec-2018	03-Jul-2024	28-Jun-2024
IDA-D3210	Effective	05-Jun-2018	16-Oct-2018	08-Jan-2019	03-Jul-2024	30-Jun-2026
IDA-D3260	Closed	05-Jun-2018	27-Jun-2018	20-Dec-2018	03-Jul-2024	28-Jun-2024

8. KEY DATES

Key Events	Planned	Actual
Approval	05-Jun-2018	05-Jun-2018
Effectiveness	09-Nov-2018	09-Nov-2018
Mid-Term Review No. 01	31-Mar-2022	09-May-2022
Mid-Term Review No. 02	06-May-2024	06-May-2024
Operation Closing/Cancellation	30-Jun-2026	

9. RESTRUCTURING HISTORY

Restructuring Level 2 Approved on 28-Jun-2024

Restructuring Level 2 Approved on 30-Jun-2022

10. ASSOCIATED OPERATION(S)

There are no associated operations
