



Congo Digital Acceleration Project (P175592)

WESTERN AND CENTRAL AFRICA | Congo, Republic of | IBRD/IDA | Investment Project Financing (IPF) | FY 2022 | Seq No: 6
| Archived on 30-Jun-2025 | ISR04209

1. OBJECTIVE

1.1 Development Objective

Original Development Objective (Approved as part of Approval package on 02-Jun-2022)

The PDO is (i) to increase broadband internet access to underserved populations, and (ii) to improve public sector's capacity to deliver digitally enabled public services.

Has the Development Objective been changed since Board Approval of the Project Objective?

No

2. COMPONENTS

Name
Component 1. Strengthening the Enabling Environment for Digital Transformation Acceleration:(Cost 17,500,000.00)
Component 2. Expanding and Increasing Digital Broadband Connectivity and Digital Inclusion:(Cost 42,500,000.00)
Component 3. Improving Delivery of, and Access to People-centric Digitally Enabled Public Services:(Cost 33,000,000.00)
Component 4. Project Management, Monitoring, and Evaluation:(Cost 7,000,000.00)
Component 5. Contingent Emergency Response:(Cost 0.00)

3. OVERALL RATINGS

Name	Previous	Current
Progress towards achievement of PDO	● Satisfactory	● Satisfactory
Overall Implementation Progress (IP)	● Moderately Satisfactory	● Moderately Satisfactory
Overall Risk Rating	● Substantial	● Substantial

4. KEY ISSUES & STATUS



4.1 Implementation Status and Key Decisions

The Congo Digital Acceleration Project was declared effective as of January 12, 2023. Following a period of delay in the implementation of activities between August 2024 and March 2025, the project has made significant progress in the implementation of activities. Overall, the project is making progress in strengthening digital infrastructure with the connection of 12 ministries, agencies and the University. Meanwhile, the project is in the process of improving its fiduciary management, and to accelerate the implementation of environmental and social safeguard activities to ensure the successful implementation. Finally, the recruitment of the new project coordinator is pending but expected to be finalized soon. The project has reached a disbursement rate of 36% as of June 9, 2025 compared to 16% in December 2024, showing the significant progress achieved to date.

5. SYSTEMATIC OPERATIONS RISK-RATING TOOL

Risk Category	Rating at Approval Approval Package - 02 Jun 2022	Last Approved Rating ISR Seq. 05 - 24 Dec 2024	Proposed Rating
Political and Governance	● Substantial	● Substantial	● Substantial
Macroeconomic	● High	● High	● High
Sector Strategies and Policies	● Moderate	● Moderate	● Moderate
Technical Design of Project or Program	● Moderate	● Moderate	● Moderate
Institutional Capacity for Implementation and Sustainability	● Substantial	● Substantial	● Substantial
Fiduciary	● Substantial	● High	● Substantial
Environment and Social	● Substantial	● Substantial	● Substantial
Stakeholders	● Moderate	● Moderate	● Moderate
Other	● Substantial	● Substantial	● Substantial
Overall	● Substantial	● Substantial	● Substantial



6. RESULTS

6.1 PDO Indicators by PDO Outcomes

Increased broadband internet access to underserved populations								
Indicator Name	Baseline		Actual (Previous)		Actual (Current)		Closing Period	
	Value	Month/Year	Value	Date	Value	Date	Value	Month/Year
People using broadband internet (new use) (Number of people) CRI	0	Mar/2025					81,000	Dec/2027
People using broadband internet (new use) - Female (Number of people) CRI	0	Mar/2025					41,000	Dec/2027
People using broadband internet (new use) - Youth (Number of people) CRI	0	Mar/2025					28,000	Dec/2027
People using broadband internet (inferred use) (Number of people) CRI	0	Mar/2025					130,000	Dec/2027
People using broadband internet (inferred use) - Female (Number of people) CRI	0	Mar/2025					120,000	Dec/2027



People using broadband internet (inferred use) - Youth (Number of people) CRI	0	Mar/2025					90,000	Dec/2027
People using broadband internet (enhanced use) (Number of people) CRI	0	Mar/2025					303,000	Dec/2027
People using broadband internet (enhanced use) - Female (Number of people) CRI	0	Mar/2025					153,000	Dec/2027
People using broadband internet (enhanced use) - Youth (Number of people) CRI	0	Mar/2025					106,000	Dec/2027
Unique broadband subscribers per 100 inhabitants (Number)	25.00	Dec/2022	344	30-Nov-2024	344	31-May-2025	45.00	Dec/2027
	Comments on achieving targets		This indicator measures the number of unique mobile broadband subscribers per 100 inhabitants. Mobile broadband subscriptions include 3G, 4G and above (if/when launched) broadband services.					
Of which female (Percentage)	0.00		0.00		0.00		40.00	
	Comments on achieving targets		% of women who have access to broadband internet					
Improve public sector's capacity to deliver digitally enabled public services								
Indicator Name	Baseline		Actual (Previous)		Actual (Current)		Closing Period	
	Value	Month/Year	Value	Date	Value	Date	Value	Month/Year



New facilitated and digitally enabled public services available online to people citizens and businesses (Number)	0.00	Dec/2022	0.00	30-Nov-2024	0.00	31-May-2025	10.00	Dec/2027
	Comments on achieving targets		Cumulative count of the total number of new transactional e-government services available to citizens and businesses supported by the project (criminal record, extract of birth certificate, online catalog of artisan's products, etc.). The services would need to meet the standards for level 3 or level 4, as defined by the UN four-stage model of e-service maturity. See https://publicadministration.un.org/publications/content/PDFs/UN%20E-Government%20Survey%202014.pdf					
Individuals (Civil servants and government contractors) who earned certifications in foundational, intermediate, and advanced digital skills throughout the project's activities (Number)	0.00	Dec/2022	182	30-Nov-2024	238	31-May-2025	3,000.00	Dec/2027
	Comments on achieving targets		Total cumulative number of individuals, (Civil servants and government contractors) trained in digital skills or usage of digital government services who received certification at least at one training through the project (in person or virtually) — covering foundational through to highly-specialized digital skills — based on the UNESCO's DigiComp digital skills methodology.					
of which reside in rural areas (percentage) (Percentage)	0.00		0		0		40.00	
	Comments on achieving targets		The indicator is a percentage numerator: the number of government officials and contractors located in rural areas who gained certification through the project on digital skills denominator: total number of government officials and contractors who gained certification through the project on digital skills					
of which women (Percentage)	0.00		28		28		40.00	
	Comments on achieving targets		The numerator is the total number of women government officials and contractors trained and certified through the project The denominator is the individuals government officials and contractors trained under the project					

6.2 Intermediate Results Indicators by Components



Component 1. Strengthening the Enabling Environment for Digital Transformation Acceleration								
Indicator Name	Baseline		Actual (Previous)		Actual (Current)		Closing Period	
	Value	Month/Year	Value	Date	Value	Date	Value	Month/Year
(Gender informed) Congo's digital transformation strategy action plans validated and disseminated (Yes/No)	No	Dec/2022	Yes	30-Nov-2024	Yes	31-May-2025	Yes	Dec/2027
	Comments on achieving targets		Congo's digital transformation Vision 2030 strategy action plans with gender targets are validated by the National Digital Transformation Steering Committee and publicly disseminated. The Minister council should validate the strategy before September 2025.					
(Gender informed) Policy framework and regulation to enforce data protection legislation are established (Yes/No)	No	Dec/2022	Yes	30-Nov-2024	Yes	31-May-2025	Yes	Dec/2027
	Comments on achieving targets		Policies, procedures, and guidelines needed to fully implement and enforce data protection legislation are published and in force, with a dedicated agency ensuring a good course of implementation. Gender-informed refers to a framework that incorporates the impact and addresses the challenges relating to privacy invasions on women, men, and individuals of diverse sexual orientations, arising from the loss of the right to privacy, cyber harassment, discrimination in employment or other areas.					
ANSSI is operational (Yes/No)	No	Dec/2022	No	30-Nov-2024	No	31-May-2025	Yes	Dec/2027
	Comments on achieving targets		ANSSI is operating effectively, and deploys a broad range of regulatory and operational activities, from issuing regulations and verifying their application, to monitoring alert and rapid response – particularly on government networks.					
Institutes and education facilities providing government-approved courses and certification (Number)	0.00	Dec/2022	0.00	30-Nov-2024	0.00	31-May-2025	20.00	Dec/2027
	Comments on achieving targets		This indicator will count the cumulative number of institutes and education facilities providing government-approved courses and certifications through programs (both general and targeted) on basic and intermediate digital skills.					
of which in rural areas (Percentage)	0.00		0.00		0.00		50.00	
	Comments on achieving targets		the indicator is a percentage Numerator: number of institutions in rural areas providing government certified trainings denominator: number of institutions providing government certified trainings					



Trained teachers and trainers in the education system throughout the project (Number)	0.00	Dec/2022	0.00	30-Nov-2024	0.00	31-May-2025	250.00	Dec/2027
	Comments on achieving targets		Cumulative total number of teachers and trainers trained by the project through formal and informal education system, and the participating MDAs. École Polytechnique, Marien Ngouabi University, and other implementing institutes, and MDAs (i.e. Ministries of Plan, Digital Economy, Education)					
of which women (Percentage)	0.00		0.00		0.00		40.00	
	Comments on achieving targets		The indicator is a percentage numerator: number of women trainers trained through the project denominator: total number of trainers trained					
Graduates from specialized digital skills training programs reporting labor market impacts and/or better education outcomes within 12 months after the completion (Number)	0.00	Dec/2022	0.00	30-Nov-2024	0.00	31-May-2025	450.00	Dec/2027
	Comments on achieving targets		This indicator will measure the number of graduates from specialized digital skills training (such as coding bootcamps, training centers etc.) supported by the project, who reported better labor market impacts (secured new employment, increased productivity, new income), or better education outcomes within 12 months after completing targeted training with at least one training certification supported under the project. Labor market impact refers to new employment in the private sector/public sector or self-employment plus new income, and education refers to pursuing higher and/or tertiary education (e.g. specialized master’s and/or PhD programs)					
of which women (Percentage)	0.00		0.00		0.00		40.00	
	Comments on achieving targets		The indicator is a percentage Numerator: number of women graduates from specialized digital skills training programs reporting labor market impacts and/or better education outcomes within 12 months after the completion Denominator: total number of graduates from specialized digital skills training programs reporting labor market impacts and/or better education outcomes within 12 months after the completion					
Component 2. Expanding and Increasing Digital Broadband Connectivity and Digital Inclusion								
Indicator Name	Baseline		Actual (Previous)		Actual (Current)		Closing Period	



	Value	Month/Year	Value	Date	Value	Date	Value	Month/Year
Localities covered in 3G by the project (Number)	0.00	Dec/2021	0.00	30-Nov-2024	0.00	31-May-2025	212.00	Dec/2027
	Comments on achieving targets		Cumulative total number of unconnected villages and cities which become covered with 3G broadband as a result of the project					
Multimedia centers deployed in schools/post offices, according to standards to withstand climate-related shocks and natural disasters (Number)	0.00	Jan/2022	0.00	30-Nov-2024	0.00	31-May-2025	132.00	Dec/2027
	Comments on achieving targets		Cumulative total number of multimedia centers setup/deployed and operationalized in the rural areas either in schools, post offices, etc. The infrastructure to be built is subject to quality standards, including compliance with disaster response requirements and climate change adaptation.					
MDAs connected to fiber by the project (Number)	0.00	Dec/2021	12	30-Nov-2023	13	31-May-2025	22.00	Dec/2027
	Comments on achieving targets		This indicator will count the number of MDAs connected to both fiber by the project, and in which users can access the internet. MDAs could also include research and innovation agencies, or higher education institutions					
People provided with new or enhanced access to broadband internet (Number)	0.00	Dec/2022	48,500	30-Nov-2024	48,500	31-May-2025	1,500,000.00	Dec/2027
People provided with new or enhanced access to broadband internet – Female (Number)	0.00		0.00		0.00		600,000.00	
Private sector investment mobilized through the project (Amount(USD))	0.00	Dec/2022	0.00	30-Nov-2024	0.00	31-May-2025	12,000,000.00	Dec/2027
	Comments on achieving targets		Private sector investment contribution mobilized through the project to finance ICT infrastructure development					
Component 3. Improving Delivery of, and Access to People-centric Digitally Enabled Public Services								
Indicator Name	Baseline		Actual (Previous)		Actual (Current)		Closing Period	



	Value	Month/Year	Value	Date	Value	Date	Value	Month/Year
People using digitally enabled services (Number of people) CRI	0	Mar/2025	0	30-Nov-2024	0	31-May-2025	706,000	Dec/2027
People using digitally enabled services – Youth (Number of people) CRI	0	Mar/2025	0	30-Nov-2024	0	31-May-2025	355,000	Dec/2027
People using digitally enabled services – Female (Number of people) CRI	0	Mar/2025	0	30-Nov-2024	0	31-May-2025	247,000	
CR and ID legal and regulatory framework modernized (Yes/No)	No	Dec/2021	No	30-Nov-2024	No	31-May-2025	Yes	Dec/2027
	Comments on achieving targets		The Civil Registration and ID legislation updated, approved by the Parliament, and disseminated.					
Digital ID roadmap and operational plan drafted (Yes/No)	No	Dec/2021	No	30-Nov-2024	No	31-May-2025	Yes	Dec/2027
	Comments on achieving targets		The Government defined the strategic roadmap of the modernization of the digital ID system and drafted the operational plan.					
Operationalization of digitalized CR database (Yes/No)	No	Dec/2022	No	30-Nov-2024	No	31-May-2025	Yes	Dec/2027
	Comments on achieving targets		A national digital database of CR records is operational.					
Average unique daily access to digital services developed under the project (Number)	0.00	Dec/2022	0.00	30-Nov-2023	0.00	31-May-2025	75,000.00	Dec/2027
	Comments on achieving targets		The indicator measures the daily average number of unique access to all digital services- informational and transactional - (GtoC and GtoB) financed under the project, over a period of one calendar year.					
Share of users satisfied with the eGov one-stop-shop portal (Percentage)	0.00	Dec/2021	0.00	30-Nov-2024	0.00	31-May-2025	70.00	Dec/2027
	Comments on achieving targets		Numerator: Number of users facilitated in the use of government services available online through the one-stop-shop portal supported by this project providing feedback and					



			expressing at least moderate satisfaction with said services. Denominator: Total number of users facilitated in the use of government services available online through the one-stop-shop portal supported by this project providing feedback. Indicator is not cumulative and should be calculated based on feedback recorded in the preceding year of implementation. The indicator will be measured through surveys embedded in the service portal. This will take the form of online questionnaires that will be sent out to users for completion, comprising of qualitative questions designed by the user-experience research group in order to inform the enhancement's cycle of the portal on an annual basis and future development of digital government services b the product/service provider and the portal management unit.					
People consulted or involved in the design and delivery of digitally enabled public services (Number)	0.00	Dec/2021	0.00	30-Nov-2024	101	31-May-2025	1,000.00	Dec/2027
	Comments on achieving targets		This indicator will count the number of people consulted through virtual or in-person focus group, interviews and surveys, or participated in user research process on the design and delivery of e-services to be financed under the project as part of e.g. the process re-engineering of a given e-service, or selection or e-services to prioritize for digitization/upgrade. The indicator will be measured by collating cumulative numbers for each of the sessions the objective of which to gather inputs and feedback on services prioritization and design. Data collected will directly shape e-services to enable wider access and usage.					
of which percentage of women (Percentage)	0.00		0.00		0		50.00	
	Comments on achieving targets		share of all people consulted in the design of systems that are women					
Number of Public Data Centers upgraded (Number)	0.00	Dec/2022	0.00	30-Nov-2024	0.00	31-May-2025	2.00	Dec/2027
	Comments on achieving targets		This indicator will count the number of public Data Centers upgraded under the project.					




Component 4. Project Management, Monitoring, and Evaluation								
Indicator Name	Baseline		Actual (Previous)		Actual (Current)		Closing Period	
	Value	Month/Year	Value	Date	Value	Date	Value	Month/Year
Grievances addressed within the stipulated service standards for response times (Percentage)	0.00	Dec/2021	75	30-Nov-2024	80	31-May-2025	90.00	Dec/2027
	Comments on achieving targets		Numerator: Cumulative number of grievances responded to/addressed within the stipulated service standards for response time. Denominator: Cumulative total number of grievances received. Service standards including response times will be defined in the Project Implementation Manual.					



7. DATA ON FINANCIAL PERFORMANCE

7.1 Cumulative Disbursements

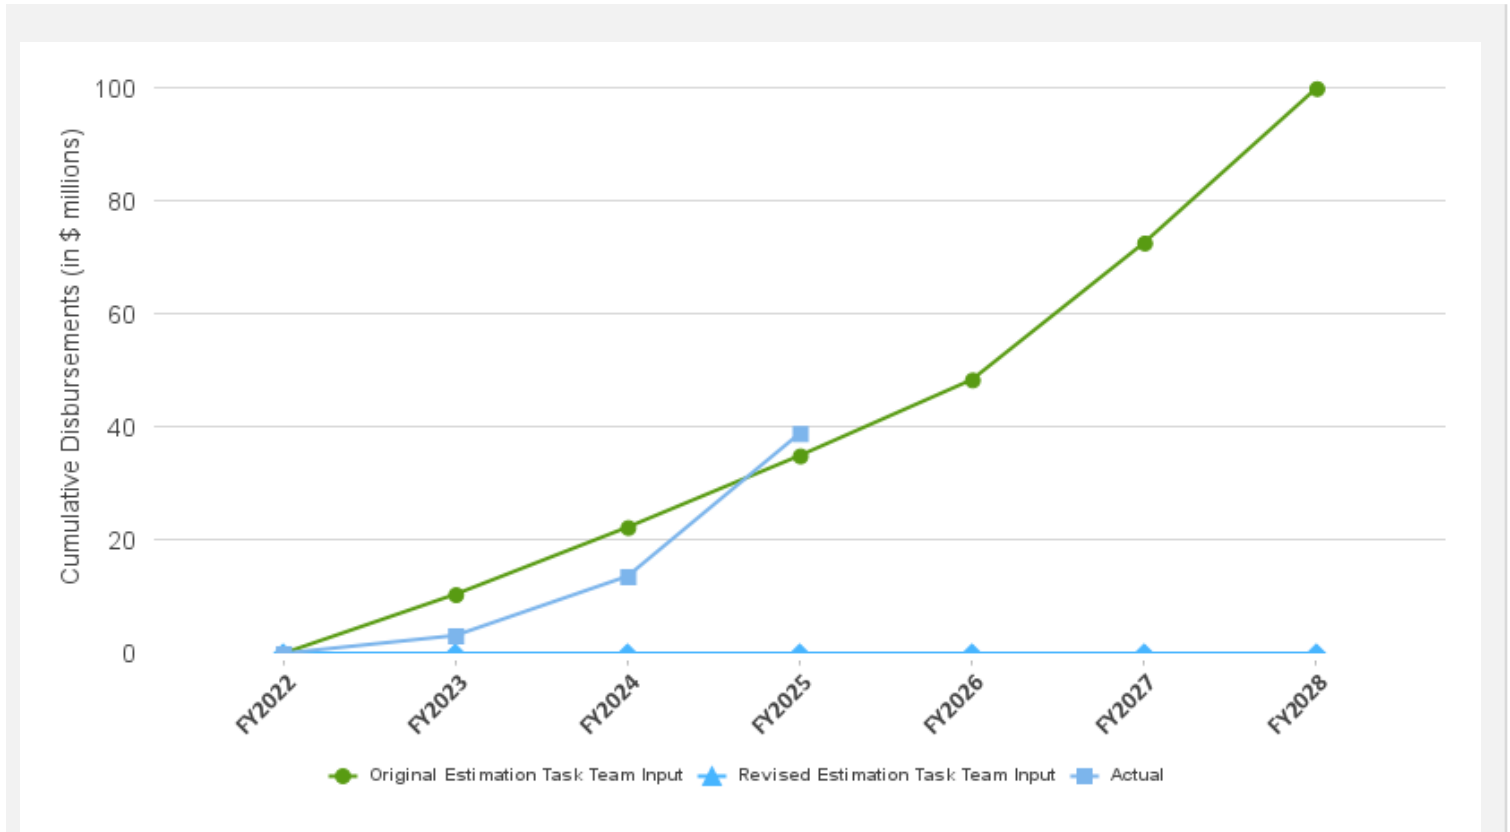

7.2 Disbursements (by loan)

Loan/Credit/TF	Status	Original	Revised	Cancelled	Disbursed	Undisbursed	% Disbursed
IBRD-93980	Effective	100.00	100.00	0.00	39.19	60.81	39.19%

7.3 Key Dates (by loan)

Loan/Credit/TF	Status	Approval	Signing	Effectiveness	Orig. Closing	Rev. Closing
IBRD-93980	Effective	02-Jun-2022	23-Jun-2022	12-Jan-2023	31-Dec-2027	31-Dec-2027

8. KEY DATES



Key Events	Planned	Actual
Approval	02-Jun-2022	02-Jun-2022
Effectiveness	12-Jan-2023	12-Jan-2023
Mid-Term Review No. 01	29-Sep-2025	
Operation Closing/Cancellation	31-Dec-2027	

9. RESTRUCTURING HISTORY

10. ASSOCIATED OPERATION(S)

There are no associated operations
