



Burkina Faso Digital Acceleration Project (P177022)

WESTERN AND CENTRAL AFRICA | Burkina Faso | IBRD/IDA | Investment Project Financing (IPF) | FY 2024 | Seq No: 4 |
Archived on 28-Dec-2025 | ISR06425

1. OBJECTIVE

1.1 Development Objective

Original Development Objective (Approved as part of Approval package on 23-Jan-2024)
The PDO is (i) to expand access to affordable broadband, (ii) to improve access to and adoption of selected digitally enabled public services, and (iii) to increase access to digital skills programs.
Has the Development Objective been changed since Board Approval of the Project Objective?
No

2. COMPONENTS

Name
Component 1. Expanding Digital Connectivity?for?Digital Inclusion?:(Cost 57,000,000.00)
Component 2. Accelerating the Digital Transformation of Public Services for Inclusion and Universal Accessibility:(Cost 64,000,000.00)
Component 3. Developing Digital Skills for the Knowledge Economy:(Cost 22,000,000.00)
Component 4. Project Management:(Cost 7,000,000.00)
Component 5. Contingent Emergency Response Component (CERC):(Cost 0.00)

3. OVERALL RATINGS

Name	Previous	Current
Progress towards achievement of PDO	● Satisfactory	● Satisfactory
Overall Implementation Progress (IP)	● Satisfactory	● Satisfactory
Overall Risk Rating	● Substantial	● Substantial



4. KEY ISSUES & STATUS

4.1 Implementation Status and Key Decisions

The Burkina Faso Digital Acceleration Project (PACTDIGITAL), approved on January 23, 2024, and effective since September 19, 2024, reflects progress observed during the third implementation support mission (December 8–12, 2025).

Progress has been made across several key components:

- Component 1 – Connectivity: Procurement for rural broadband connectivity is in its final stage. Awarded operators will begin deployment upon contract signing and issuance of the notice to proceed.
- Component 2 – Digital Government: Progress includes development and deployment of platforms such as e-Patient and the Justice system’s administrative legal proceedings platform, operational since December 15, 2025.
- Component 4 – Citizen Engagement: The grievance mechanism and annual consultations with citizens are operational and recording initial statistics.
- Institutional Arrangements: PIU is fully operational. Most legal covenants are fulfilled, with the remaining covenant under preparation.

All relevant stakeholders have actively contributed to the planning process. To ensure effective implementation, bi-monthly follow-up meetings with the World Bank team, have been established.

5. SYSTEMATIC OPERATIONS RISK-RATING TOOL

Risk Category	Rating at Approval Approval Package - 23 Jan 2024	Last Approved Rating ISR Seq. 03 - 30 Jun 2025	Proposed Rating
Political and Governance	● High	● High	● High
Macroeconomic	● Substantial	● Substantial	● Substantial
Sector Strategies and Policies	● Substantial	● Substantial	● Substantial
Technical Design of Project or Program	● Substantial	● Substantial	● Substantial



Institutional Capacity for Implementation and Sustainability	● Substantial	● Substantial	● Substantial
Fiduciary	● Substantial	● Moderate	● Moderate
Environment and Social	● Substantial	● Substantial	● Substantial
Stakeholders	● Substantial	● Substantial	● Substantial
Overall	● Substantial	● Substantial	● Substantial



6. RESULTS

6.1 PDO Indicators by PDO Outcomes

To expand access to affordable broadband								
Indicator Name	Baseline		Actual (Previous)		Actual (Current)		Closing Period	
	Value	Month/Year	Value	Date	Value	Date	Value	Month/Year
People using broadband internet (new use) (Number of people) CRI	0	Oct/2023	0	23-Jun-2025	0	15-Dec-2025	3,000,000	Aug/2028
	Comments on achieving targets		The procurement process is in its final stage, and the awarded operators will begin deploying the localities immediately upon contract signing and issuance of the notice to proceed.					
People using broadband internet (new use) - Female (Number of people) CRI	0	Oct/2023	0	23-Jun-2025	0	15-Dec-2025	1,350,000	Aug/2028
People using broadband internet (new use) - Youth (Number of people) CRI	0	Oct/2023	0	23-Jun-2025	0	15-Dec-2025	2,000,000	Aug/2028
People using broadband internet (inferred use) (Number of people) CRI					0	15-Dec-2025		Aug/2028
People using broadband internet (inferred use) - Female (Number of people) CRI					0	15-Dec-2025		Aug/2028



People using broadband internet (inferred use) - Youth (Number of people) CRI					0	15-Dec-2025		Aug/2028
People using broadband internet (enhanced use) (Number of people) CRI					0	15-Dec-2025		Aug/2028
	Comments on achieving targets		The procurement process is in its final stage, and the awarded operators will begin deploying the localities immediately upon contract signing and issuance of the notice to proceed.					
People using broadband internet (enhanced use) - Female (Number of people) CRI					0	15-Dec-2025		Aug/2028
People using broadband internet (enhanced use) - Youth (Number of people) CRI					0	15-Dec-2025		Aug/2028
People provided with new or enhanced access to broadband internet (Number)	0.00	Oct/2023	0.00	09-Dec-2024	0.00	15-Dec-2025	3,000,000.00	Aug/2028
	Comments on achieving targets		This is a data at the time the initial ISR. The project is not effective yet and no change in the RF has been recorded.					
People provided with new or enhanced access to broadband internet – Female (Number)	0.00		0.00		0.00		1,350,000.00	
	Comments on achieving targets		This is a data at the time the initial ISR. The project is not					
Average monthly price of a 5-GB internet subscription (Amount(USD))	13.02	Oct/2023	13.02	09-Dec-2024	13.02	15-Dec-2025	4.88	Aug/2028
	Comments on achieving targets		Retail price of mobile broadband sub-basket, prepaid handset-based, 5 GB (3G and above), in US\$.					



To improve access to and adoption of selected digitally enabled public services								
Indicator Name	Baseline		Actual (Previous)		Actual (Current)		Closing Period	
	Value	Month/Year	Value	Date	Value	Date	Value	Month/Year
People benefiting from digitally enabled public services supported by the project (Number)	0.00	Oct/2023	0.00	23-Jun-2025	0.00	15-Dec-2025	3,000,000.00	Aug/2028
	Comments on achieving targets		Quantity of individuals who have accessed and benefited from public services that have been enhanced through digital. It aims to assess the reach and impact of initiatives that leverage digital platforms, tools, and processes to improve the delivery of public services. The indicator focuses on the number of people who have utilized digitally enhanced public services, such as Patient electronic medical records, Entrance competitions and professional examinations for the public administration or Administrative and legal proceedings. These services are designed to provide convenience, efficiency, and accessibility to citizens, enabling them to access and interact with public services in a more streamlined and user-friendly manner.					
of which female (Percentage)	0.00		0.00		0.00		40.00	
	Comments on achieving targets		which female access to digital public services					
Public institutions buildings connected to broadband and facilitating access to digitally enabled public services (Number)	0.00	Oct/2023	0.00	23-Jun-2025	0.00	15-Dec-2025	400.00	Aug/2028
	Comments on achieving targets		Number of Public institutions buildings connected to RESINA supported by the project.					
To increase access to digital skills programs								
Indicator Name	Baseline		Actual (Previous)		Actual (Current)		Closing Period	
	Value	Month/Year	Value	Date	Value	Date	Value	Month/Year
People provided with digital skills programs supported by the project (Number)	0.00	Oct/2023	0.00	23-Jun-2025	0.00	15-Dec-2025	1,277,500.00	Aug/2028
	Comments on achieving targets		Cumulative number of individuals benefiting directly from digital skills programs at all levels supported by the project under Component 3 benefitting either in-person, virtually or with a					



		hybrid approach. This indicator will include beneficiaries ranging from digital literacy to basic, intermediate, advanced and digital entrepreneurship programs.
of which female (Percentage)	0.00	0.00
	Comments on achieving targets	Supplemental indicator

6.2 Intermediate Results Indicators by Components

Component 1. Expanding Digital Connectivity?for?Digital Inclusion?								
Indicator Name	Baseline		Actual (Previous)		Actual (Current)		Closing Period	
	Value	Month/Year	Value	Date	Value	Date	Value	Month/Year
Burkina Faso's eWaste strategy adopted and implemented by GoBF (Yes/No)	No	Oct/2023	No	09-Dec-2024	No	15-Dec-2025	Yes	Aug/2028
	Comments on achieving targets	Key metrics of verification are: (a) eWaste strategy adopted by GoBF; and (b) Extended Producer Responsibility (EPR) program set-up and operational.						
Unique broadband subscribers per 100 inhabitants (gender disaggregated) (Percentage)	41.00	Oct/2023	41.00	09-Dec-2024	41.00	15-Dec-2025	50.00	Aug/2028
	Comments on achieving targets	Number of unique mobile broadband subscribers per 100 inhabitants. Mobile broadband subscriptions include 3G, 4G and above (if/when launched) broadband services.						
of which female (Percentage)	25.00		25.00		25.00		40.00	
	Comments on achieving targets	Percentage of women who have access to broadband internet						
of which reside in rural areas (Percentage)	54.00		54.00		54.00		60.00	
	Comments on achieving targets	Percentage of unique broadband subscribers per 100 inhabitants located in rural areas						
	0.00	Oct/2023	0.00	09-Dec-2024	0.00	15-Dec-2025	335.00	Aug/2028



Fiber optic deployed (Kilometers)	Comments on achieving targets		Number of kilometers of fiber optic cables deployed by the project as part of the national backbone.					
MDAs with new or enhanced broadband by the project (Number)	0.00	Oct/2023	0.00	09-Dec-2024	0.00	15-Dec-2025	20.00	Aug/2028
	Comments on achieving targets		Cumulative number of MDAs with new or enhanced broadband connectivity by the project. MDAs could also include research and innovation agencies, higher education institutions or digital centers hosted in town halls, office posts, community centers (e.g. youth or citizens).					
Newly built or upgraded digital infrastructure that is resilient to climate related shocks (Number)	0.00	Oct/2023	0.00	09-Dec-2024	0.00	15-Dec-2025	90.00	Aug/2028
	Comments on achieving targets		The newly built and upgraded broadband infrastructure under this project will be subject to quality standards that include compliance with the requirements for disaster response and for climate change mitigation (to be elaborated in bidding documents). These requirements will include, for example, the usage of weather-resistant materials, waterproof coverings, and underground infrastructure with climate-resilient design to withstand floods.					
Localities covered in 3G or 4G by the project (Number)	0.00	Sep/2023	0.00	09-Dec-2024	0.00	15-Dec-2025	250.00	Aug/2028
	Comments on achieving targets		Cumulative total number of unconnected villages and cities which become covered with 3G or 4G broadband as a result of the project					
Value of private sector investment leveraged under the project (Amount(USD))	0.00	Oct/2023	0.00	09-Dec-2024	0.00	15-Dec-2025	23,500,000.00	Aug/2028
	Comments on achieving targets		Private sector investment in digital infrastructure and services leveraged in response to project supported activities.					
Component 2. Accelerating the Digital Transformation of Public Services for Inclusion and Universal Accessibility								
Indicator Name	Baseline		Actual (Previous)		Actual (Current)		Closing Period	
	Value	Month/Year	Value	Date	Value	Date	Value	Month/Year
People using digitally enabled services (Number of people) CRI			0	09-Dec-2024	0	15-Dec-2025		
People using digitally enabled services – Youth (Number of people) CRI			0	09-Dec-2024	0	15-Dec-2025		



People using digitally enabled services – Female (Number of people) CRI			0	09-Dec-2024	0	15-Dec-2025		
The Digital Services Portal is rebuilt on a people-centric service-based model (Yes/No)	No	Oct/2023	No	15-Apr-2024	No	15-Apr-2024	Yes	Aug/2028
	Comments on achieving targets		Key metrics of verification are: (a) system will have the capability to expose services and consume services with other systems; (b) omnichannel and allow different forms of service delivery channels such as through web-based portal, Mobile App etc; (c) user feedback management system and help desk operational.					
Patients with an active electronic medical record in the public health system (Number) (Number)	0.00	Oct/2023	0.00	15-Apr-2024	0.00	15-Apr-2024	2,800,000.00	Sep/2028
	Comments on achieving targets		Cumulative number of individuals who have an electronic medical record that is currently active and accessible within the public health system.					
of which female (Percentage)	0.00		0.00		0.00		50.00	
	Comments on achieving targets		supplemental indicator					
Files related to administrative legal proceedings of the Justice system that have been digitized by the project (Percentage)	0.00	Oct/2023	0.00	15-Apr-2024	0.00	15-Apr-2024	50.00	Aug/2028
	Comments on achieving targets		The administrative legal proceedings platform of the Justice system developed under the project has been operational since Monday, December 15, 2025 (official launch): https://justice-penale.gov.bf . Online files submission will begin on January 15, 2026.					
Candidates participating in digitized entrance competitions and professional examinations (Number)	0.00	Oct/2023	0.00	15-Apr-2024	0.00	15-Apr-2024	1,000,000.00	Aug/2028
	Comments on achieving targets		Quantity of individuals who engage in the digitized process of entrance competitions and professional examinations. It reflects the level of interest and participation in the newly implemented digital system, indicating the extent to which candidates are utilizing the simplified and accessible procedures.					
	0.00	Oct/2023	0.00	15-Apr-2024	0.00	15-Apr-2024	30.00	Aug/2028



World Bank projects-financed systems, platforms, databases that are hosted on secure hosting solutions (Number)	Comments on achieving targets		Number of WB projects-financed systems, platforms, databases that are hosted on secure hosting solutions.					
Government staff and contractors trained in digital skills and in digital economy policies supported under the project (Number)	0.00	Oct/2023	0.00	15-Apr-2024	0.00	15-Apr-2024	4,000.00	Aug/2028
	Comments on achieving targets		Cumulative number of government staff and contractors trained in digital skills.					
Burkina Faso’ digital transformation strategy with a gender and PWDs lens updated and adopted by GoBF (Yes/No)	No	Oct/2023	No	15-Apr-2024	No	15-Apr-2024	Yes	Aug/2028
	Comments on achieving targets		Burkina Faso’ digital transformation strategy with a gender and PWDs lens updated and adopted by the GoBF					
Component 3. Developing Digital Skills for the Knowledge Economy								
Indicator Name	Baseline		Actual (Previous)		Actual (Current)		Closing Period	
	Value	Month/Year	Value	Date	Value	Date	Value	Month/Year
Beneficiaries completing digital literacy training programs under the project (Number)	0.00	Oct/2023	0.00	09-Dec-2024	0.00	09-Dec-2024	1,200,000.00	Aug/2028
	Comments on achieving targets		Digital literacy training will support digital inclusion among the general population particularly the most vulnerable groups and contribute to increased adoption of public e-services as well as other innovative private platforms among the newly connected beneficiaries to broadband services under Component 1. In partnership with community-based organizations, this program will equip women, out-of-school youth, IDPs and PWDs with adequate skills to improve access to information that can improve beneficiaries’ productivity, employability and livelihood.					
of which female (Percentage)	0.00		0.00		0.00		50.00	
	Comments on achieving targets		Supplemental indicator					



of which reside in rural areas (Percentage)	0.00		0.00		0.00		40.00	
	Comments on achieving targets		Supplemental indicator					
Beneficiaries completing intermediate and advanced digital skills training under the project (Number)	0.00	Oct/2023	0.00	09-Dec-2024	0.00	15-Dec-2025	61,500.00	Aug/2028
	Comments on achieving targets		Basic digital skills training aimed at national education students and teachers especially as part of emergency response through the learning continuity through digital project (sub-component 3.2.a). These activities may include, but not limited to, learning how to navigate a desktop computer, move and edit files, finding information on the internet, social media, and online safety. Intermediate digital skills, include, but are not limited to, digital marketing, graphic design, or social media management. While advanced and specialized digital skills might include software development, cloud computing, Internet of Things, big data, artificial intelligence, and cybersecurity among other priority areas. This indicator would also include the number of students attending the public high schools with STEM vocation which benefit from the project's support to provide research, innovation, and technology related services and courses to enable students address local challenges through digital.					
of which female (Percentage)	0.00		0.00		0.00		40.00	
	Comments on achieving targets		of which are female					
Share of individuals trained in intermediate or advanced digital skills who report new or improved employment or increase in income 6 to 12 months after	0.00		0.00		0.00		50.00	
	Comments on achieving targets		Trainees with new employment, a promotion or expanded responsibilities in their current employment, or an increase in self-reported income through formal employment, freelancing, or online work 6 to 12 months after completing the training.					




completing the training. (Percentage)								
Digital entrepreneurs who received advanced/specialized training and/or technical support under the project (Number)	7,750.00	Oct/2023	7,750.00	09-Dec-2024	7,750.00	15-Dec-2025	16,000.00	Aug/2028
	Comments on achieving targets		Digital entrepreneurs who are participating and receive support from ESOs, which might include, but is not limited to, business development services, soft skills training, mentorship, networks, and support to access new markets.					
of which female (Percentage)	0.00		0.00		0.00		30.00	
	Comments on achieving targets		Supplemental indicator					
Component 4. Project Management								
Indicator Name	Baseline		Actual (Previous)		Actual (Current)		Closing Period	
	Value	Month/Year	Value	Date	Value	Date	Value	Month/Year
Grievances responded to and/or addressed within the stipulated service standards for response times (Percentage)	0.00	Oct/2023	0.00	09-Dec-2024	100.00	15-Dec-2025	90.00	Aug/2028
	Comments on achieving targets		Percentage of grievances or complaints relating to the project, which are addressed within the stipulated service standards for response time. Service standards including response times will be defined in the Project Implementation Manual.					
Annual consultations with citizens, users of digital government platforms, and civil society to solicit feedback and report on actions taken to address feedback since previous consultations (Number)	0.00	Oct/2023	0.00	09-Dec-2024	2.00	15-Dec-2025	5.00	Aug/2028
	Comments on achieving targets		Annual consultations in the form of workshops, research, or similar outreach to stakeholders of project-supported platforms – including public sector decision makers, public sector end users, civil society organizations, beneficiaries and members of the population at large, including representation of a wide variety of marginalized groups – which solicit feedback from said stakeholders on the design and implementation of project-supported activities and report on action taken as a result of prior consultations. Reports shuld be publicly disclosed.					



7. DATA ON FINANCIAL PERFORMANCE

7.1 Cumulative Disbursements

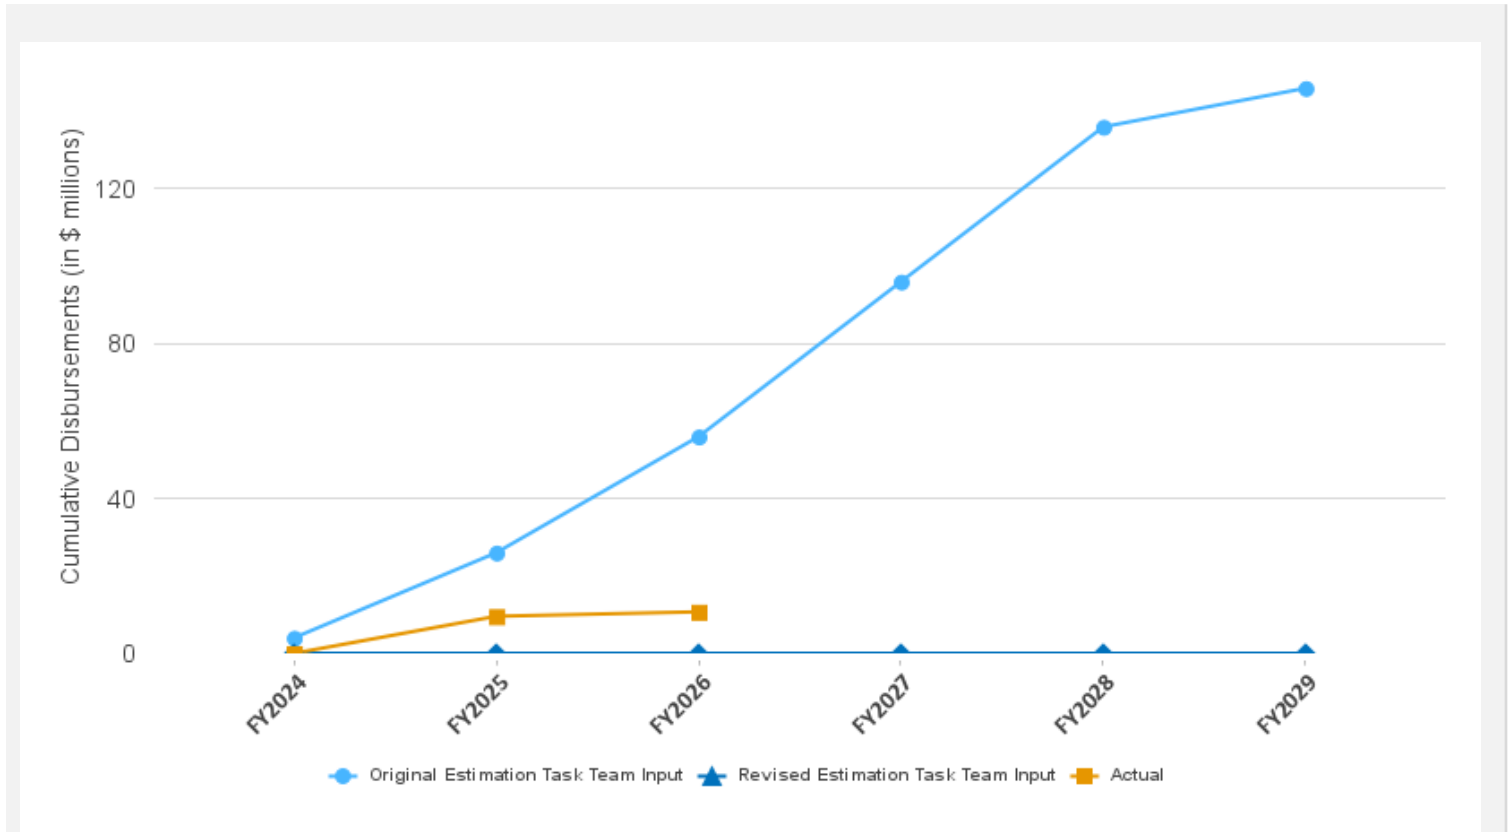

7.2 Disbursements (by loan)

Loan/Credit/TF	Status	Original	Revised	Cancelled	Disbursed	Undisbursed	% Disbursed
IDA-74620	Effective	150.00	166.13	0.00	10.73	154.46	6.50%

7.3 Key Dates (by loan)

Loan/Credit/TF	Status	Approval	Signing	Effectiveness	Orig. Closing	Rev. Closing
IDA-74620	Effective	23-Jan-2024	14-Feb-2024	19-Sep-2024	30-Nov-2028	30-Nov-2028

8. KEY DATES



Key Events	Planned	Actual
Approval	23-Jan-2024	23-Jan-2024
Effectiveness	19-Sep-2024	19-Sep-2024
Operation Closing/Cancellation	30-Nov-2028	

9. RESTRUCTURING HISTORY

10. ASSOCIATED OPERATION(S)

There are no associated operations
